

WR-61928416
WO-17316369
FEEDER: R-26-NY & R-27-NY (36KV)
L-1-QN-L (13.2KV)

SUB-TX WORK TO BE COMPLETED ON:
WR-62937495
WO-17921519


SCHEDULER NOTE:
-NO TRUCK ACCESS TO 4 POLES:
CXE-837206, CXE-837207, CXE-837208 & CXE-837209
-TRACK DIGGER NEEDED

RECORDS NOTE:
From Loc 002 to Loc 006:
- EXISTING 1-1/0 PRIMARY & 1-1/0 NEUTRAL TO REMAIN
- ADD ADDITIONAL 2-1/0 PRIMARY TO SPANS

WIRE NOTES:
BET Loc 001 AND Loc 006:
- INST 2-1/0 PRIMARY (1600'EA)
BET Loc 006 & Loc 009:
- INST 3-1/0 PRIMARY AND 1-1/0 NEUTRAL (660'EA)
BET Loc 009 & Loc 015
- INST 3-1/0 PRIMARY AND 1-1/0 NEUTRAL (950'EA)
BET Loc 015 & Loc 016
- INST 3-1/0 PRIMARY AND 1-1/0 NEUTRAL (50'EA)

ILLUM CO FORESTRY NOTE:
TRIM FOR ADDITIONAL FIELD
SIDE CONDUCTOR BET Loc 001
and Loc 006

CUSTOMER FORESTRY NOTE:
CUT DOWN & CLEAR ALL VEGETATION
WITHIN ROAD R/W BETWEEN
BET Loc 006 and Loc 009

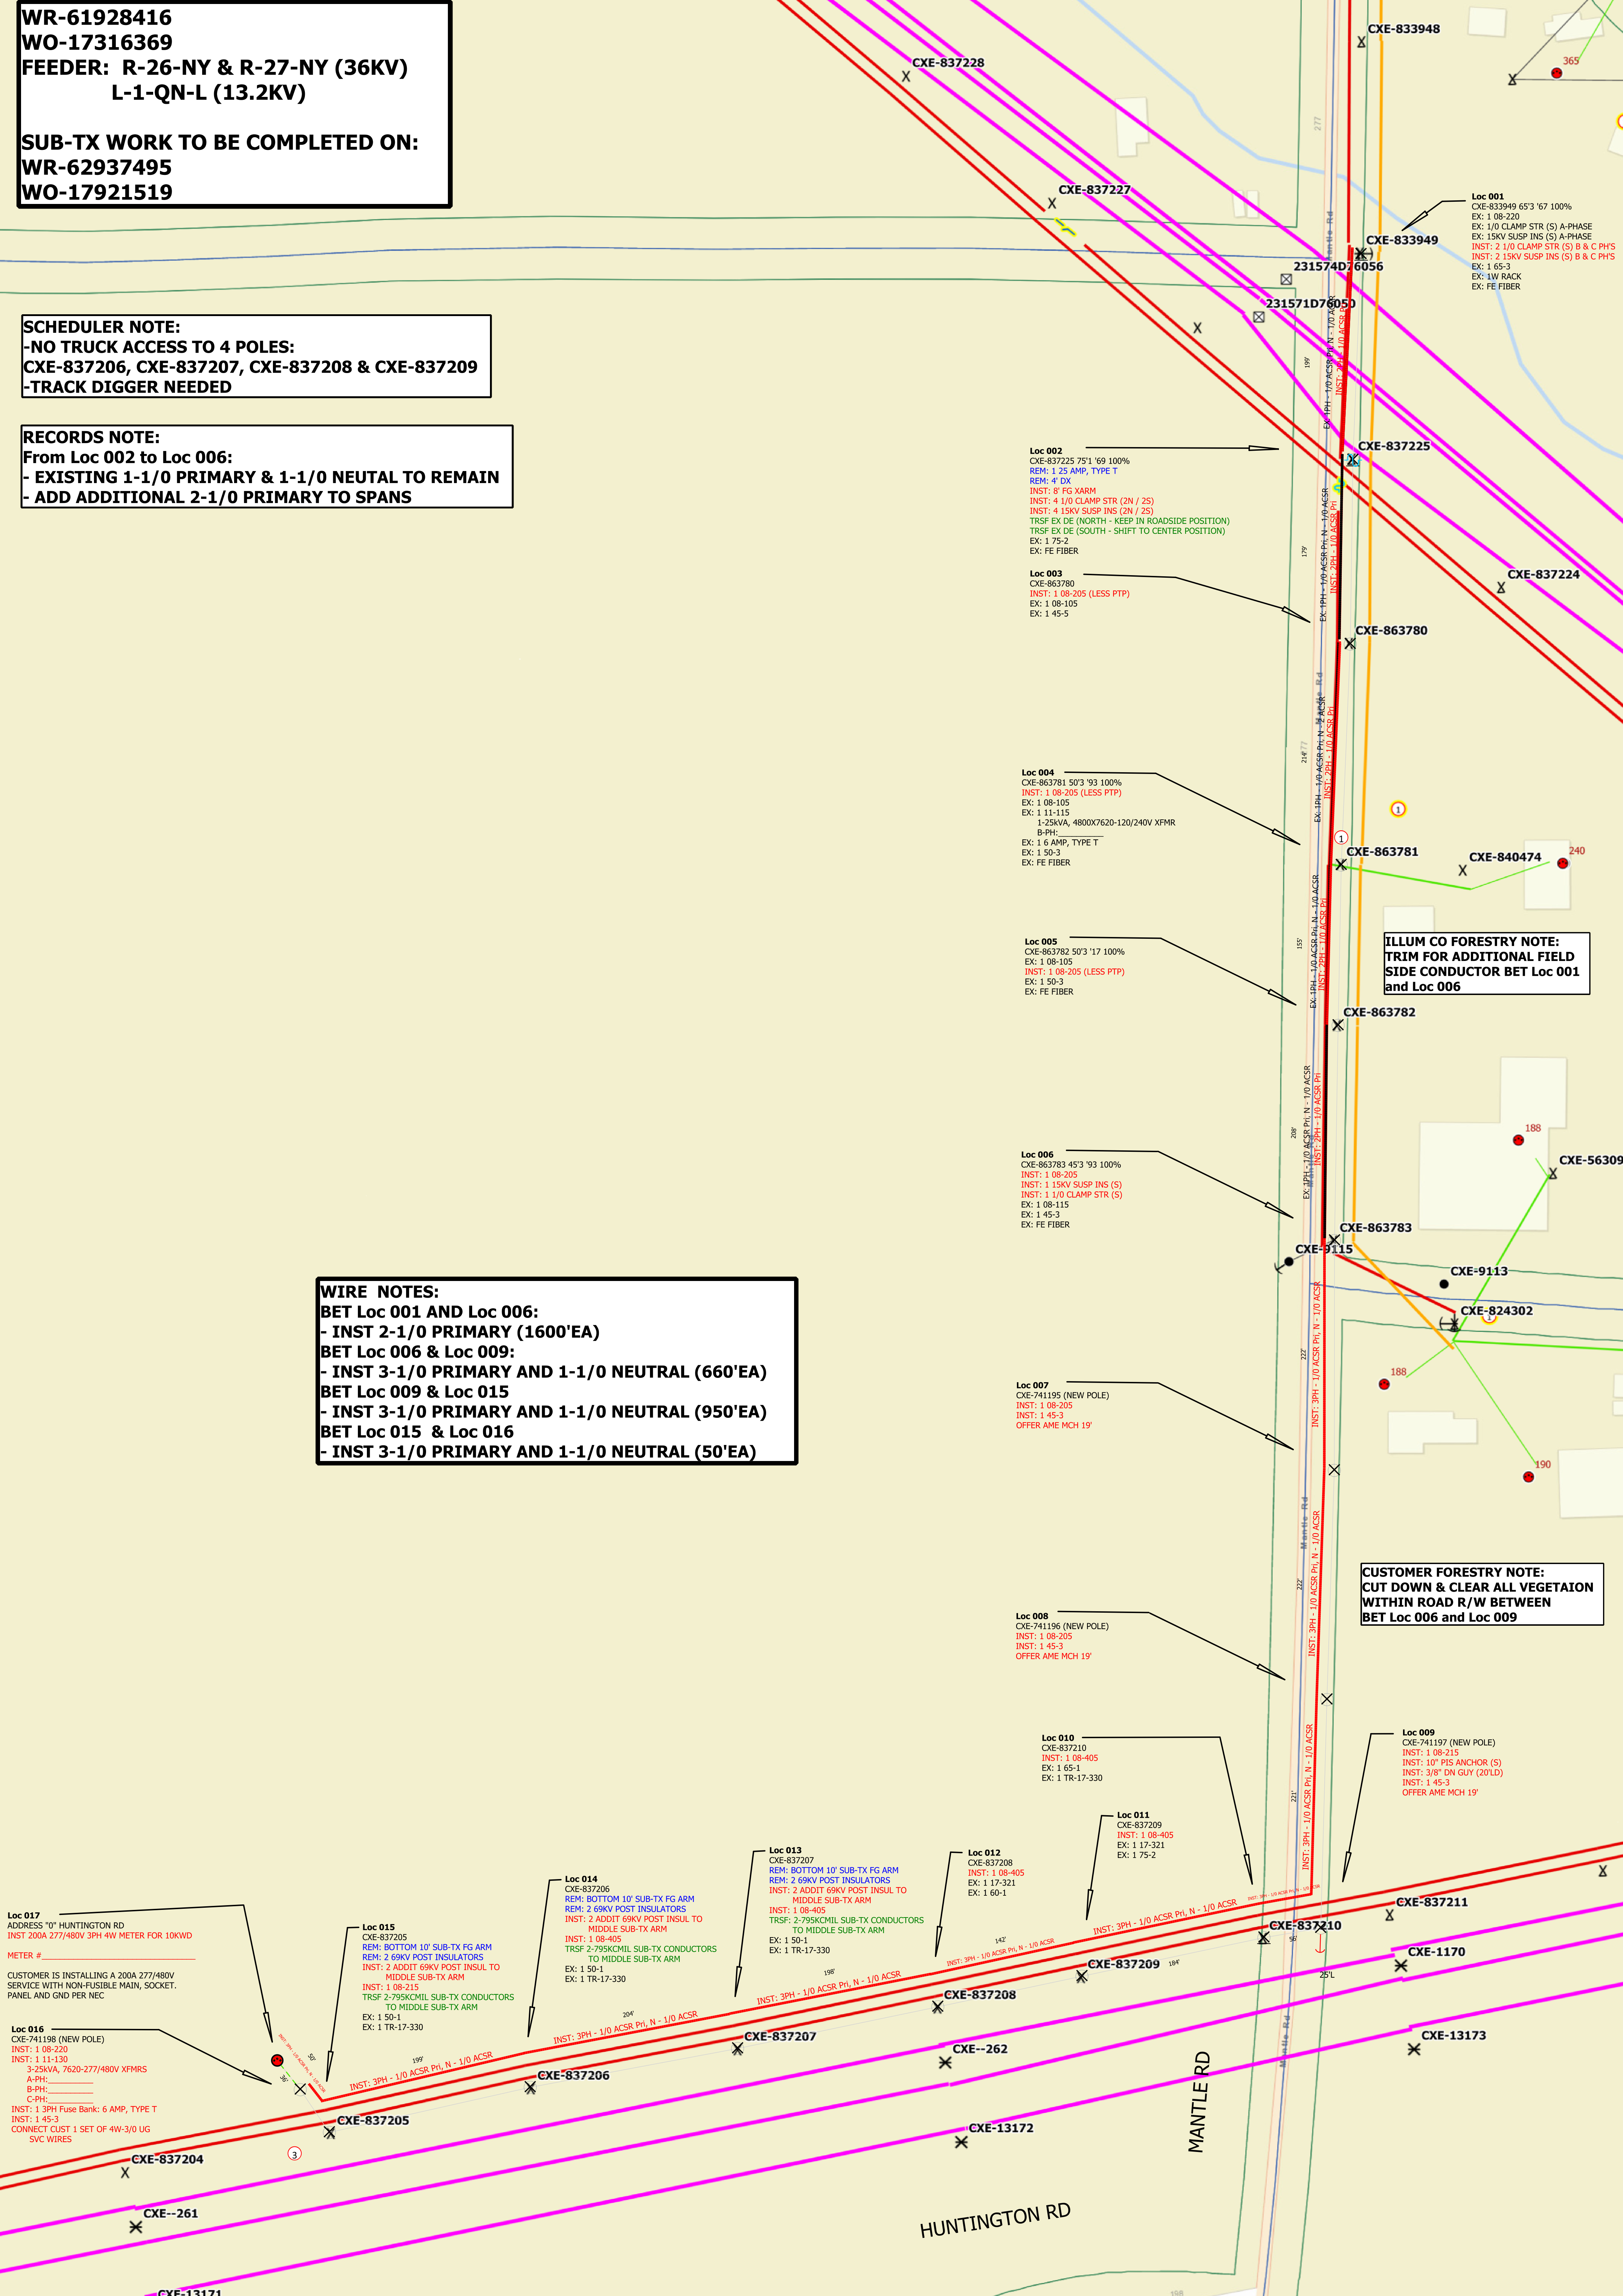

WR#: 61928416	SAP Order #: 17316369	Req ISD: 4/1/2024	Print Date: 12/1/23
Street Address: 0 HUNTINGTON RD	City, State Zip: PAINESVILLE, OH 44077	State One Call#: 1-800-362-2784 or 811	Project #:
Sub/Circ: QN L001QN	Upstream Prot Device: CXE-833946	Designer: Weir Gary L. (440)358-4928	J/J Proposal #:
Customer: LAKE COUNTY DEPT OF UTILITIES, (440)350-2324	Construction Foreman Signature: _____ Date: _____	Approver: <i>Dylan Long</i> 12/1/2023	Cust Elec: _____
Notes/Comments:		Date:	

Forest Joint Use Sheet 1 of 1
 REV: CREWS Revision 2 Scale 1:67
